I hereby certify that this document and the data contained herein were prepared by me or under my direct supervision.

Steven J. Thompson — Date: 4-16-25

Registration No. 22705

☒ Land Surveyor, ☐ Professional Engineer
☐ County Surveyor, ☐ County Engineer

MOWER COUNTY COORDINATES
NAD 83 (96) HARN
Northing=N140868.07 Latitude=N043°36'30.808373"
Easting=E738558.30 Longitude=W093°02'57.708596"

A687780

Office of the County Recorder
Mower County, Minnesota

I HEREBY CERTIFY THE WITHIN INSTRUMENT WAS FILED, AND/OR RECORDED ON 5/20/2025 8:44 AM

PACKAGE: 108345 REC FEE: $0.00

Sara Madison, Mower County Recorder

CERTIFICATE OF LOCATION OF GOVERNMENT CORNER

W1/4 Corner of Section 30, Township 102N Range 18W, 5th P.M.

STATE OF MINNESOTA, County of MOWER


At the corner location shown on the sketch

☐ On 2/10/2025 (DATE) found a NOTHING

☒ left monument as found, ☐ lowered monument, ☐ removed monument (explain)

☐ On 2/10/2025 (DATE) placed a SET 5/8"Ø REBAR CAPPED #22705

SKETCH OF REFERENCE TIES

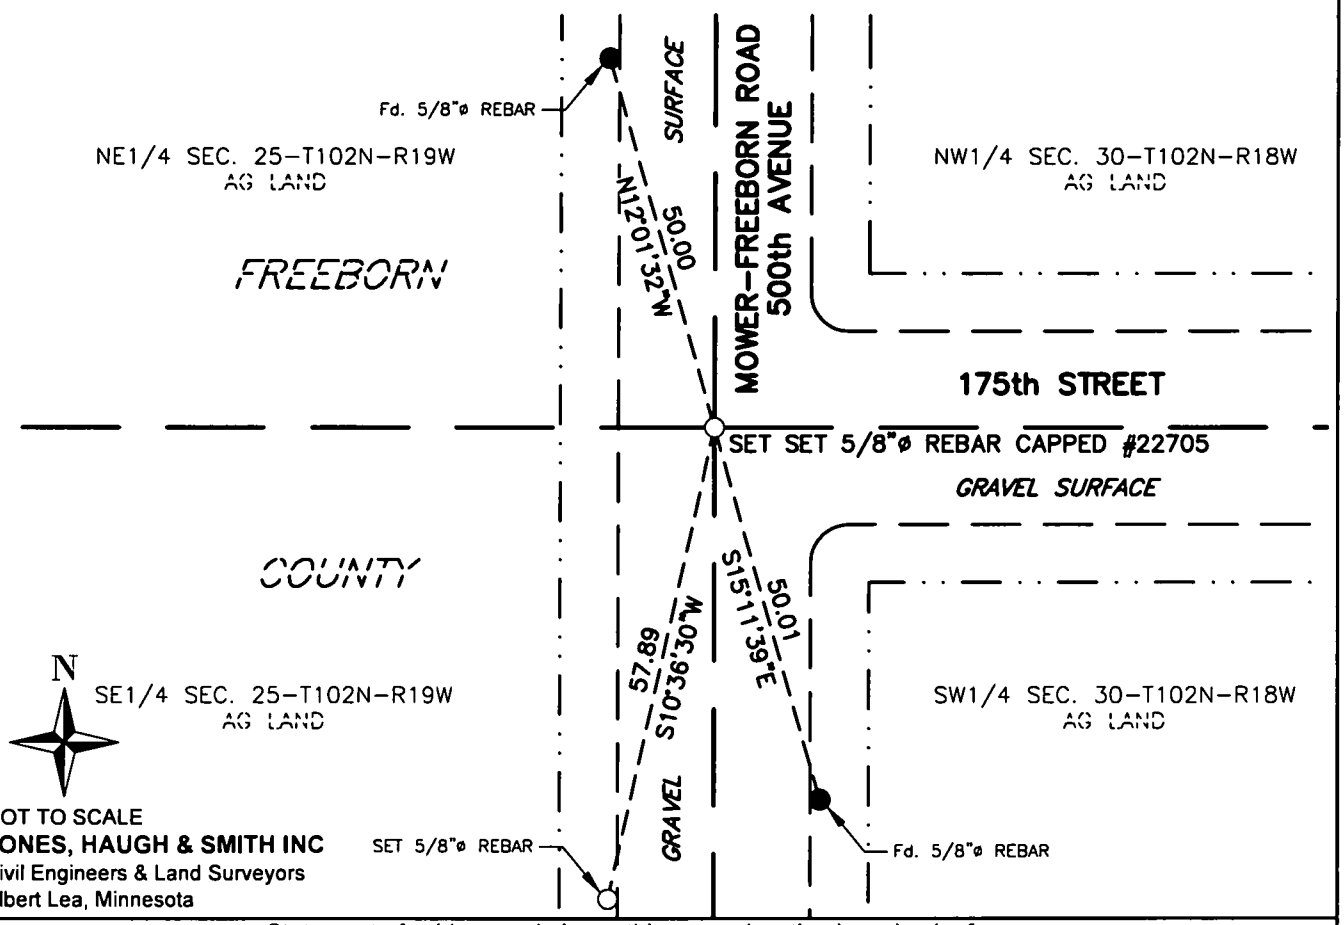

NOT TO SCALE

JONES, HAUGH & SMITH INC
Civil Engineers & Land Surveyors
Albert Lea, Minnesota

Statement of evidence relative to this corner location is on back of page.

STATEMENT OF EVIDENCE

W1/4 Corner Section 30-T102N-R18W

This corner was established by Deputy Surveyor J.B. Reyman in May-July, 1854. The government notes show a wood post was set and mound with trench and pits per instructions.

September 7, 1995: Jones, Haugh, & Smith crew set corner using government distances. Proportional distance from NE corner Section 24 to SE corner Section 25. Proportional distance being 2639.56 between section corners. Set 5/8" x 16" iron with cast iron monument. Fits centerline of township road east and 2'± west of centerline N-S of township road.

February 10, 2025: Jones, Haugh, & Smith crew searched corner location and found nothing. Reset 5/8"Ø rebar capped 22705 using NW tie, SE tie & NE corner of Section 25 and made ties.

For electronic survey data and analysis, contact the firm of Jones, Haugh and Smith Inc.


SJ


MINIMUM
MAINTENANCE
ROAD

